

Options Appraisal

A. PROJECT SUMMARY INFORMATION

Project Name:	Winsley CC
Lead Officer (Sponsor):	N MacDougall
Report lead author(s):	W Griffiths , N MacDougall, Simon Richards
Report recipients:	Winsley CC Exec Committee

B. ORGANISATIONAL CONTEXT

Alignment to corporate theme(s):	Winsley Cricket Club Development Plan: 2024 to 2026
Project category:	☐ Saving delivery ☐ Compliance / Statutory ☒ Risk reduction ☒ Cost avoidance ☒ Improved outcomes ☒ Enabling

C. DOCUMENT CONTROL

Document status:	Final
Document owner:	N MacDougall

Version	Author(s)	Description	Date
V00_01	N MacDougall	First draft	30/3/26
V00_02	Simon Richards	2 nd Draft	28/4/26
V00_03	2 nd Pitch team comment	3 rd draft	4/5/26
<V1_00>	Niall MacDougall	<FINAL SIGNED OFF VERSION>	7 May 26

Executive Summary

1. As requested by The Winsley Executive Committee (WEC) an outline option and cost analysis has been completed by the 2nd Pitch Project team (2PPT).
2. The only viable ground for a second pitch in the parish of Winsley was at BOA RFC option 3 in the initial report at the far eastern part of the ground.
3. BOA RFC are content for the ground to be there and opposition to the cricket club and from BAWCASA has been overcome after 4 years of engagement.
4. BOA RFC would be content to offer a 50 year lease if BOAWCASA granted that term to the Rugby club.
5. Both the 2PPT and BOA RFC have a target of signing an agreement by Xmas 2026 and the first cut of the turf in April 2027 with the ground ready to play its first match in June 2029.
6. Therefore 2PPT offer 5 options for the WEC to consider and choose one to take forward to the membership. These are intended to be modular so that the ground can develop over time by enhancing the playing area and facilities
7. These will range from option 1 a do nothing proposal whereby the club would seek a long term lease with Southwick Sports Club to option 5 which is do everything such as build a pavilion and have enhanced work completed on the wicket and outfield.

8. A range of external funding options will also be provided.

9. A caveat to this paper is that 2PPT will not be held accountable for the prices provided as the team believe that the project is not ready to provide firm pricing to WEC as it has not carried out the necessary diligence in securing pricing nor has a requirement been received from WEC to guide 2PPT towards a preferred solution. Discussion of this paper should solve the latter.

10. 2PPT would like agreement for the following :

a. An initial budget of £1500 for a survey of the proposed ground and give advice to inform the best Course of Action. This will be chosen from Ecosolve, Total Play and STRI Group.

b. To draw up a letter of intent for the rugby club to set out the requirements and high level terms that Winsley CC would need and find acceptable to proceed. This letter would be non-binding and subject to contract.

c. WEC to decide which option they wish to take forward for membership approval

Assumptions

1. Winsley CC ExCO is committed to this project and supportive of 2PPT.

2. All prices are fixed and would need to be validated by normal procurement processes ie 3 quotes. 3. Winsley CC will sub-let through BOA RFC.

4. The Sub lease will be signed by Christmas 2026.

5. Work on the 2nd pitch will begin in the Spring of 2027.

6. The wicket will take 24 months to bed in before it is fit to play.

7. Grounds equipment at Southwick will be transferred to the Winsley CC at BOA RFC.

8. The grounds committee will take on the construction and maintenance of the ground from Spring 2027.

9. The grounds committee will manage the maintenance of BOA RFC using volunteers from the club. 10. A water supply is adjacent to the proposed pitch.

11. Funding will be achieved using ECB grants and loans as well as external grants such as the county lottery and Hills reclamation. The project will try to avoid using Winsley CC reserves.

12. The project is designed to be modular and could be completed over several phases.

13. Winsley CC 3rds and 4ths will play at BOA RFC on a Saturday and WEC are content that they are suitable over at least 10 years.

14. Winsley CC U11s and 15s teams will play at BOA RFC on a Monday.

15. A number of Sunday friendly games [unspecified] will be played at BOA RFC. 16. A number of women's softball and hardball pairs games [unspecified] will play

at BOA RFC 17. U15 and Softball women's training may take place at BOA RFC on a Friday or Tuesday. 18. Once WEC have agreed an option to be taken forward

this will be presented to the membership.

Winsley CC and BOA RFC Relationship

1. Discussions for a 2nd pitch at BOA RFC have been ongoing for about 4 years

2. There was some tension between both clubs due to the laying of an artificial pitch at BOA RFC whereby Winsley CC declined to use it despite an investment put into the ground by BAWCASA.

3. BOA RFC would prefer WINSLEY CC to use another part of the ground but this is deemed unsuitable by 2PPT.

4. Both parties have now agreed the area for a 2nd pitch.

5. BAWCASA have verbally agreed to waive any historical payments they believe are due from Winsley CC as they invested in the ground and Winsley CC declined to use it.

6. BOA RFC would like a joint (non-binding) letter of intent to move the process forward.

7. BOA RFC agree that work should start in the Spring of 2027 with an agreement being signed in December 2026.

8. BOA RFC are content for a 50 year lease and to split the legal costs 3 ways. 9. The relationship between both parties is excellent with both clubs supporting the others events. 10. A risk to choosing option 1 (see below) would be a significant deterioration to this relationship.

11. This could jeopardise Winsley CC aspiration to use the indoor training facility being proposed by BOA RFC in the medium term.

Options

Option 1 Do Nothing

This would be to remain at Southwick Sports Club and not to move to BOA RFC

Capital Investment	Description	Cost	Comment
Square	Not required	£0	
Outfield	Not Required	£0	
Shelter	Not Required	£0	
Machinery Accommodation	Not Required	£0	
Legal Costs	Not Required		
Equipment	Not Required		
Total	Not Required		

Resource Costs	Description	Cost	Comment
Southwick Costs	54 games at £50 a game Total £2700 Ground maint thro'out season and Renovations £4500 Southwick paid grounds workers £2730	£9930	These costs are to some extent a bench mark for the 2 nd pitch in Winsley

Option 2 Do Minimum : This would be an artificial track with the outfield having minimal work to make it suitable for lower league cricket

Capital Investment	Description	Cost	Comment
Square	An artificial track is estimated to cost between £10k & 15K for this option a figure of £12.5k is considered	£12500	
Outfield	This will be rolled and mown as well as quadriplayed	£400	Winsley CC volunteers will do this
Shelter	A shelter (summerhouse) with a built in shed will cost £2400 delivered	£2400	

Machinery Accommodation	See above a summer house with a built in shed are on the market and will be adequate for this option (paint, Brushes, Square frame , boundary roller and markers etc)	£0	
Legal Costs	BOA RFC estimate that legal costs will be 10k and propose that they are split 3 ways	£3300	
Equipment	Its is assumed equipment will be inherited from the Southwick site however contingency of £500 may be prudent	£500	
Contingency	A 15% contingency may be prudent	£2865	
Total		£21965	
Resource Costs	Description	Cost	Comment
Rent	BOA RFC say rent will be in the low £00s so this is an estimate	£500	
Ground maintenance and renovation	Grass cutting £1000 Outfield renovation £1000 (seed and fertiliser)	£2000	Estimate £250 an acre cutting
Equipment maint	Estimate (or budget for £200 to renew consumables)	£200	
Total		£2700	

Option 3 Do Something

Hollow tine 6 tracks and fill with loam . Cut, roll and quadriplay the outfield basic shelter with container

Capital Investment	Description	Cost	Comment
Square	6 tracks hollow tined and filled with loam then added gradually over the years	£15000	This could be a starter and I am told by the league this track would be adequate for leagues 8 and lower. In the future 4 tracks could be improved to 4" loam in a winter
Outfield	This will be rolled and mown as well as quadriplayed	£400	Winsley CC volunteers will do this

Shelter	A shelter (summerhouse) with a built in shed will cost £2400 delivered	£2400	
Machinery Accommodation	An ISO container will cost £3000 delivered	£3000	
Legal Costs	BOA RFC estimate that legal costs will be 10k and propose that they are split 3 ways	£3300	
Equipment	Its is assumed equipment will be inherited from the southwick site however contingency of £500 may be prudent	£500	
Contingency	A 15% contingency may be prudent	£3690	
Total		£28290	
Resource Costs	Description	Cost	Comment
Rent	BOA RFC say rent will be in the low £00s so this is an estimate	£500	
Ground maintenance and renovation	Grass cutting £1000 Outfield renovation £1000 (seed and fertiliser)	£2000	Estimate £250 an acre
Equipment maint	Estimate (or budget for £500 to renew consumables service mowers etc)	£200	
Total		£2700	

Option 4 Do Something (enhanced) : 6 tracks dug out with 4" loam Cut, roll and quadriplay the outfield, shelter with container

Capital Investment	Description	Cost	Comment
Square	6 tracks with 4" loam	£30000	Standard track for the Wiltshire league
Outfield	This will be rolled and mown as well as scarify, seeded and fertilised	£4000	

Shelter	A shelter (summerhouse) with a built in shed will cost £2400 delivered	£2400	
Machinery Accommodation	An ISO container will cost £3000 delivered	£3000	
Legal Costs	BOA RFC estimate that legal costs will be 10k and propose that they are split 3 ways	£3300	
Equipment	Its is assumed equipment will be inherited from the southwick site however contingency of £500 may be prudent	£500	
Contingency	A 15% contingency may be prudent	£6480	
Total		£49680	
Resource Costs	Description	Cost	Comment
Rent	BOA RFC say rent will be in the low £00s so this is an estimate	£500	
Ground maintenance and renovation	Grass cutting £1000 Outfield renovation £4000 (seed and fertiliser)	£5000	Estimate £250 an acre to cut
Equipment maint	Estimate (or budget for £500 to renew consumables service mowers etc)	£500	
Total		£6000	

Option 5 Do everything 8 tracks dug out at 6"loam with extensive work completed on the outfield Pavilion with all facilities and container for equipment

Capital Investment	Description	Cost	Comment
Square	8 Tracks at 6" loam	£55000	This would almost be HQ standard and certainly above most pitches in the lower leagues

Outfield	Full works including scarifying, fraise mowing, seeding and top dressing	£15000	
Shelter	Full pavilion with utilities (loos, electricity, water 2 changing rooms and a central space)	£24000	
Machinery Accommodation	An ISO container will cost £3000 delivered	£3000	
Legal Costs	BOA RFC estimate that legal costs will be 10k and propose that they are split 3 ways	£3300	
Equipment	Its is assumed equipment will be inherited from the southwick site however contingency of £500 may be prudent	£500	
contingency	A 15% contingency may be prudent	£15120	
Total		£115920	
Resource Costs	Description	Cost	Comment
Rent	BOA RFC say rent will be in the low £00s so this is an estimate	£500	
Ground maintenance and renovation	Grass cutting £1000 Outfield renovation £4000	£5000	Estimate £250 an acre to cut
Equipment maint	Estimate (or budget for £500 to renew consumables service mowers etc)	£500	
Total		£6000	

Funding Options

Nadeem Ahmed and Pete Mundy are tasked with looking for funding options and applying for them once the preferred option is agreed by the membership. So far the following options have been identified.

1. ECB grant - £15000 but must be primarily for Ladies or Girls cricket.
2. ECB loan – A zero interest loan is available to clubs for significant capital investment such as a second pitch. This could be £10000 and would have to be signed by WEC.
3. Wilts league grant - £300 from the Wiltshire league.
4. WEPL grant - £750+ from WEPL
5. Community Grant - £2000 from the Wiltshire community grant
6. Wiltshire council Lottery – Wiltshire County Council are launching a letter which could generate income towards this project. Amounts depend on numbers signing up
7. Winsley CC received grants from UK prosperity fund in 2026 (33k) the majority of which was used to purchase groundsman equipment for both sites.
8. BOA town council - £2000 was granted for fencing around the ground in 2020.
9. Winsley Parish Council – Winsley CC has received parish grants in the past and this could generate £1000.
10. External sources such as Hills Reclamation – a significant sum was obtained for the external nets. 11. BAWCASA – This charity may grant some funds to the project.
12. Sponsorship focus for raising funds.
13. Fund raising and donations could raise £5000

SWOT

Option 1 – Remain at Southwick

Strengths	Weaknesses
• A ground is in place that is capable of staging 3rd, 4th, ladies and youth matches • The facilities are good with a grass pitch • Ground equipment is in place to maintain ground	• Ground dislocated from Winsley CC HQ there is no need/opportunity for players to come to HQ (unlike Sulis) • Winsley CC do not have a long lease on the ground and is subject to conditions by Sports field committee at Southwick • The resource maintenance costs are very expensive (11K)
Opportunities	Threats

• Cricket is continued to be played at Southwick so a pitch is not lost. • Winsley CC investment with youth and allstars cricket may help recruitment • Winsley may be able to recruit former Beehive players	• There is a split within Winsley CC due to the dislocation leading to Beehive CC reforming. • The Southwick Sports field association decide to use the ground for other activities in the future • Some Winsley players drop out from the teams as they do not feel part of the club anymore due to the dislocation
---	--

Option 2 – Artificial at BOA RFC

Strengths	Weaknesses
• This is a quick cheap option and means that the ground could be used from 2027 and maintenance is low. • Grass tracks could be added at a later stage to enhance the facilities • The ground is close to HQ so keeps all teams of the club together	• Most players do not like playing on an artificial pitch • Winsley CC will be sub-letting to BOA RFC and whilst a long lease is mooted the club could be vulnerable • A capital investment to prepare the ground to a suitable playing area
Opportunities	Threats
• Closer relationship with BOA RFC whereby ideas and support are shared • May recruit BOA RFC players • Have a 2nd ground which is close to HQ and has the opportunity to expand thus strengthening the cricket clubs offer.	• Winsley CC cannot sustain 2 league sides and junior sides to make the ground viable • The artificial track takes some time to order and therefore opportunity is lost • Winsley players do not want to play there

Option 3 – Hollow tine 6 Tracks

Strengths	Weaknesses
• This is a quick cheap option and adequate for lower Wilts league games (league 8 or lower) • 4" Grass tracks could be added at a later stage to enhance the playing area ie 3 over one winter and another 3 a couple of winters later • The ground is close to HQ so keeps all teams of the club together	• The pitch will take time to develop and may not be the best playing surface for several years • Winsley CC will be sub-letting to BOA RFC and whilst a long lease is mooted the club could be vulnerable. • The ground will take 2 years to prepare before ready to play
Opportunities	Threats

• Closer relationship with BOA RFC whereby ideas and support are shared • May recruit BOA RFC players • Have a 2nd ground which is close to HQ and has the opportunity to expand thus strengthening the cricket clubs offer.	• Winsley CC cannot sustain 2 league sides and junior sides to make the ground viable • There is a capital cost for this option and there is not an established playing surface • Winsley players do not want to play there as the playing surface is deemed too poor and take too long to get to a suitable standard
---	---

Option 4 – 4” loam track with a total of 6 tracks

Strengths	Weaknesses
• This is the ideal playing surface for lower league and junior games • Players will want to play on this surface • The ground is close to HQ so keeps all teams of the club together and cohesive	• The pitch will take time to develop and may not be the best playing surface for several years. The ground will take 2-3 years to prepare before ready to play • Winsley CC will be sub-letting to BOA RFC and whilst a long lease is mooted the club could be vulnerable. • There is a substantial capital investment required for this option (£46k)
Opportunities	Threats
• Closer relationship with BOA RFC whereby ideas and support are shared • May recruit BOA RFC players • Have a 2nd ground which is close to HQ and has the opportunity to expand thus strengthening the cricket clubs offer.	• Winsley CC cannot sustain 2 league sides and junior sides to make the ground viable • The capital investment does not enhance the clubs playing offer • The ground takes too long to establish itself and the players lose interest due the time delay

Option 5 – 6” loam track total of 8 tracks

Strengths	Weaknesses
• This is the ideal playing surface for and would rival the playing conditions at HQ • Players will want to play on this surface • The ground is close to HQ so keeps all teams of the club together and cohesive	• The ground will take 2-3 years to prepare before ready to play • Winsley CC will be sub-letting to BOA RFC and whilst a long lease is mooted the club could be vulnerable. • There is a substantial capital investment required for this option (£110k)

Opportunities	Threats
• Closer relationship with BOA RFC whereby ideas and support are shared • May recruit BOA RFC players • Have a 2nd ground which is close to HQ and has the opportunity to expand thus strengthening the cricket clubs offer.	• Winsley CC cannot sustain 2 league sides and junior sides to make the ground viable • The capital investment does not enhance the clubs playing offer • The ground takes too long to establish itself and the players lose interest due the time delay

Option Analysis

Option 1 – Option one is the status quo by remaining at Southwick. This option avoids any capital expenditure but there is a high maintenance resource cost. This option also does not fulfil Winsley CC development plan to have a 2nd pitch in the parish boundaries. This option could be discounted

Option 2 – This option is for an artificial track which is not popular with the players. However it will be the quickest way to start playing at BOA RFC. A sub option could be to combine options 2&3 or 2&4 so there is an artificial and hollow tine tracks/4” loam track which can evolve over time. This option meets the Winsley CC development plan and is the cheapest but a risk as this may not retain players. This option could be discounted.

Option 3 – This option is to hollow tine 6 tracks and gradually build up the quality of the square over time. This maybe unattractive to players but there is the carrot of the ground improving. Groundsmen have said this is fine for lower Wilts league games. A sub option would be to combine this with option 2 or with Option 4 to save money. This option has been attempted unsuccessfully at Winsley CC HQ in the past and the grounds team advised that it should not be taken forward.


Option 4 – This option is for 6 x 4” loam tracks which would be optimal for Wilts league pitches. This meets Winsley CC Development plan aspirations and could attract players. There is also a possibility of a sub option by combining this option with option 3 to save money and build the square up over time. This is 2PPT preferred option.

Option 5 – This option is for 8 x 6” tracks which would mean a top quality square. The question needs to be asked is that is this necessary? This is by far the most expensive and could rival what HQ has but do we need it for league 8 or 10 cricket (although I know we have higher aspirations for the 3s) this option is could be discounted due to cost.

Options Financial Summary

	Optio n 1			Optio n 2		Option 3	Option 4	Option 5
--	--------------	--	--	--------------	--	----------	----------	----------

Do nothing			Do Minimum			Do Something			Do Something (enhanced)			Do Everything		
	ingOn	Tota		ingOn	Tota		ingOn	Tota		ingOn	Tota		ingOn	Tota

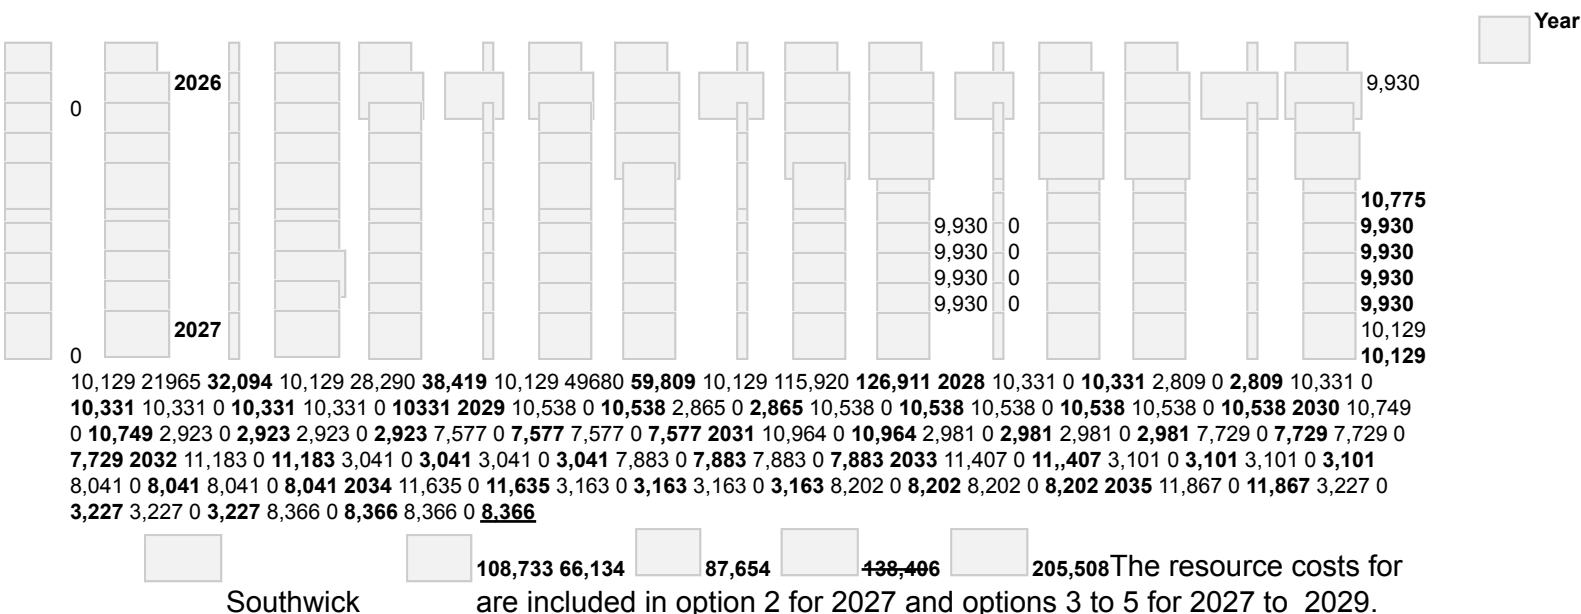

CPI is used as the inflation measure.

Recommendations for Winsley CC ExCo

1. To decide which option they wish to take forward to the membership. 2PPT will then prepare further detail for a presentation to Winsley CC membership.
2. WEC to provide a more detailed requirement for the 2nd pitch so that 2PPT can be more precise in their project plan.
3. To provide a budget of £1500 for a grounds survey with a company recommended by Wilts Cricket Ltd
4. To draw up and agree a non-binding letter of Intent to BOA RFC to move the project forward

Document sign off

Name	Title	Date circulated
Winsley Executive Committee		<DD/MM/YYYY>

Decision making authority	Winsley CC Executive Committee
Date seeking endorsement	<DD/MM/YYYY>

